


Leo Baeck Temple

Summary


Milestones & Summaries

Act ID	Description	Orig Dur	Early Start	Early Finish
G-1000	NTP	0	22SEP08 *	
G-1010	Mobilize	10	22SEP08	06OCT08
G-1200	Building & Haz Mat Investigation	10	22SEP08	06OCT08
G-1190	Project Duration - CD's	312 *	13OCT08	20AUG09
G-1210	Start Construction	0	13OCT08 *	
G-1230	Move Sactuary to (E) Social Hall	0	14APR09	
G-1220	Office/Restrooms/Utility Areas Complete	0		15MAY09
G-1160	Substantial Completion	0		20AUG09
G-1170	Punch List	15	21AUG09	11SEP09
G-1180	Final Completion	0		11SEP09

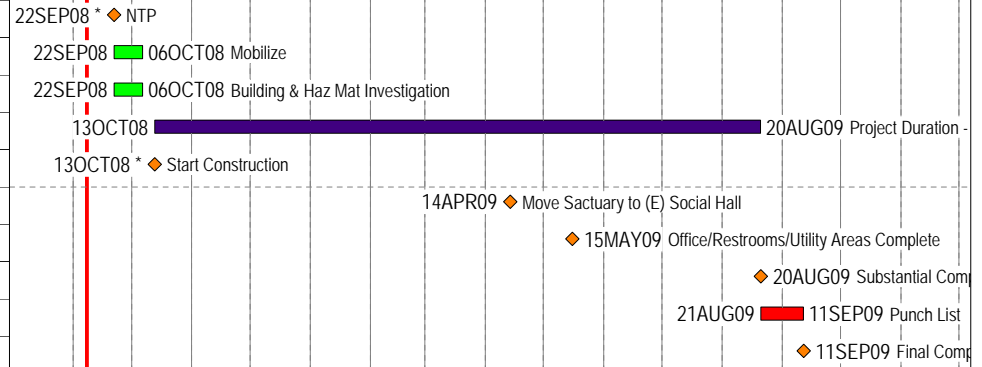


Temple Holidays & Observances

Act ID	Description	Orig Dur	Early Start	Early Finish
HO-1000	Rosh Hashanah (Tuesday)	1	30SEP08 *	30SEP08
HO-1010	Yom Kippur (Monday)	1	09OCT08 *	09OCT08
HO-1020	Sukkot (Tuesday)	1	14OCT08 *	14OCT08
HO-1030	Hanukkah (Monday)	1	22DEC08 *	22DEC08
HO-1040	Purim (Tuesday)	1	10MAR09 *	10MAR09
HO-1050	Passover (Thursday)	1	09APR09 *	09APR09
HO-1060	Rosh Hashana (Saturday)	1	19SEP09 *	19SEP09

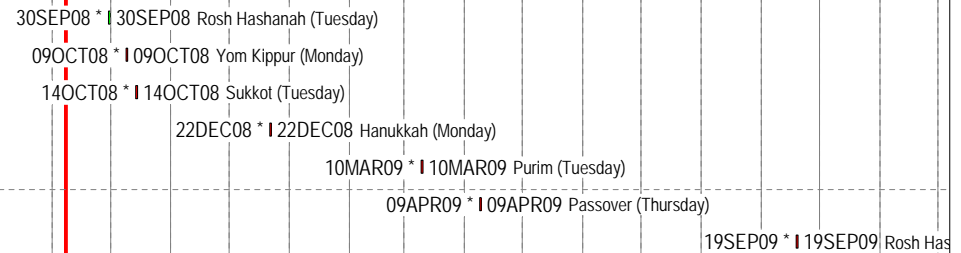

Approvals & Procurement

Act ID	Description	Orig Dur	Early Start	Early Finish
HB-1370	Approve/Procure Windows	60	22SEP08	23DEC08
HB-1090	Measure & Order Sanc/Soc Hall Oper Partition	60	28JAN09	24APR09



Construction

Low Bay Areas (Offices, Restrooms, Utility Rms)

Start date	08SEP08
Finish date	19SEP09
Data date	08SEP08
Run date	19JUN08
Page number	1A
Page count	4A
© Primavera Systems, Inc.	

